



# Project Brief - The Finn

Update # 2

June 10, 2016

745 Cleveland Avenue S.

St. Paul, MN 55116

ACKERBERG | [www.ackerberg.com](http://www.ackerberg.com) | 612.824.2100




**ACKERBERG**

## Project Partners:



## Milestone Dates:

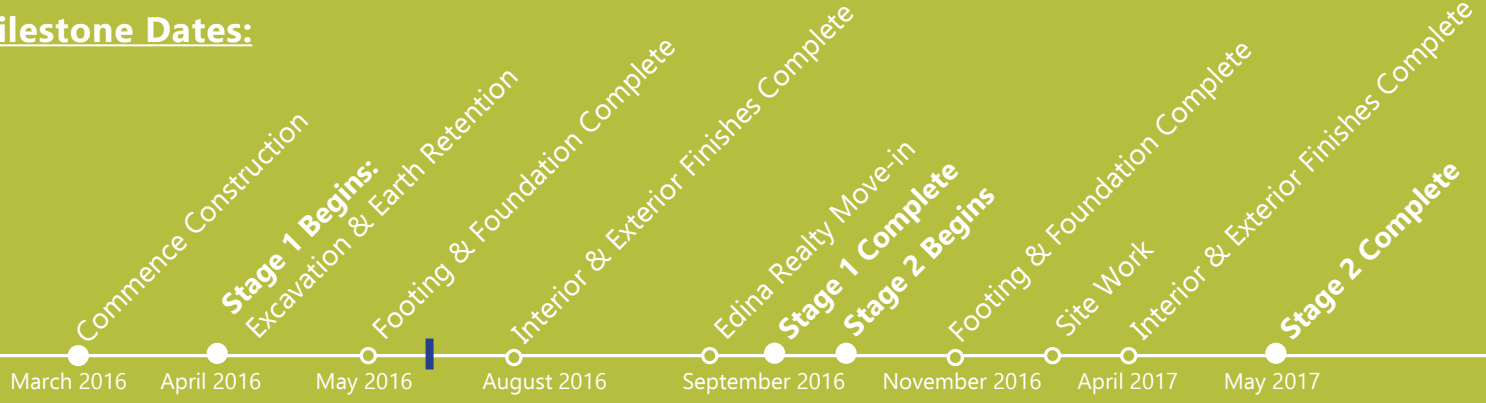

Hello Project Partners,

We hope everyone has been enjoying their summer!

Our team continues to make great strides on the construction of the first stage of The Finn. Take a look at the attached photos!

The major milestones completed to date include the completion of the excavation and temporary shoring, footings and foundations, and three levels of the elevator shafts.

Big D expects to complete installation of the precast concrete at the first and second floors as early as next week. Shortly thereafter, backfilling to the foundation walls will begin, and Big D will begin installing wood framing.

There has been a lot of activity in and around the site, and we would like to thank all of our Highland Park neighbors for their cooperation and patience.

Here's a quick look at the tasks for the coming weeks:

- Site dewatering
- Waterproofing the exterior walls
- Set elevator block walls
- Precast installation at second floor
- Setting wall panels at the main stair tower

Thank you,

Team Ackerberg



Rendering from Cleveland Ave S. (mid-block) looking northwest



**Project Start**

**Work to Date**



Cleveland Avenue and Highland Parkway



735 Cleveland Avenue, mid-block



Cleveland Avenue and Pinehurst Avenue



## Project Start



735 Cleveland Avenue, mid-block



Highland Parkway, looking south



735 Cleveland Avenue, mid-block

## Work to Date

